


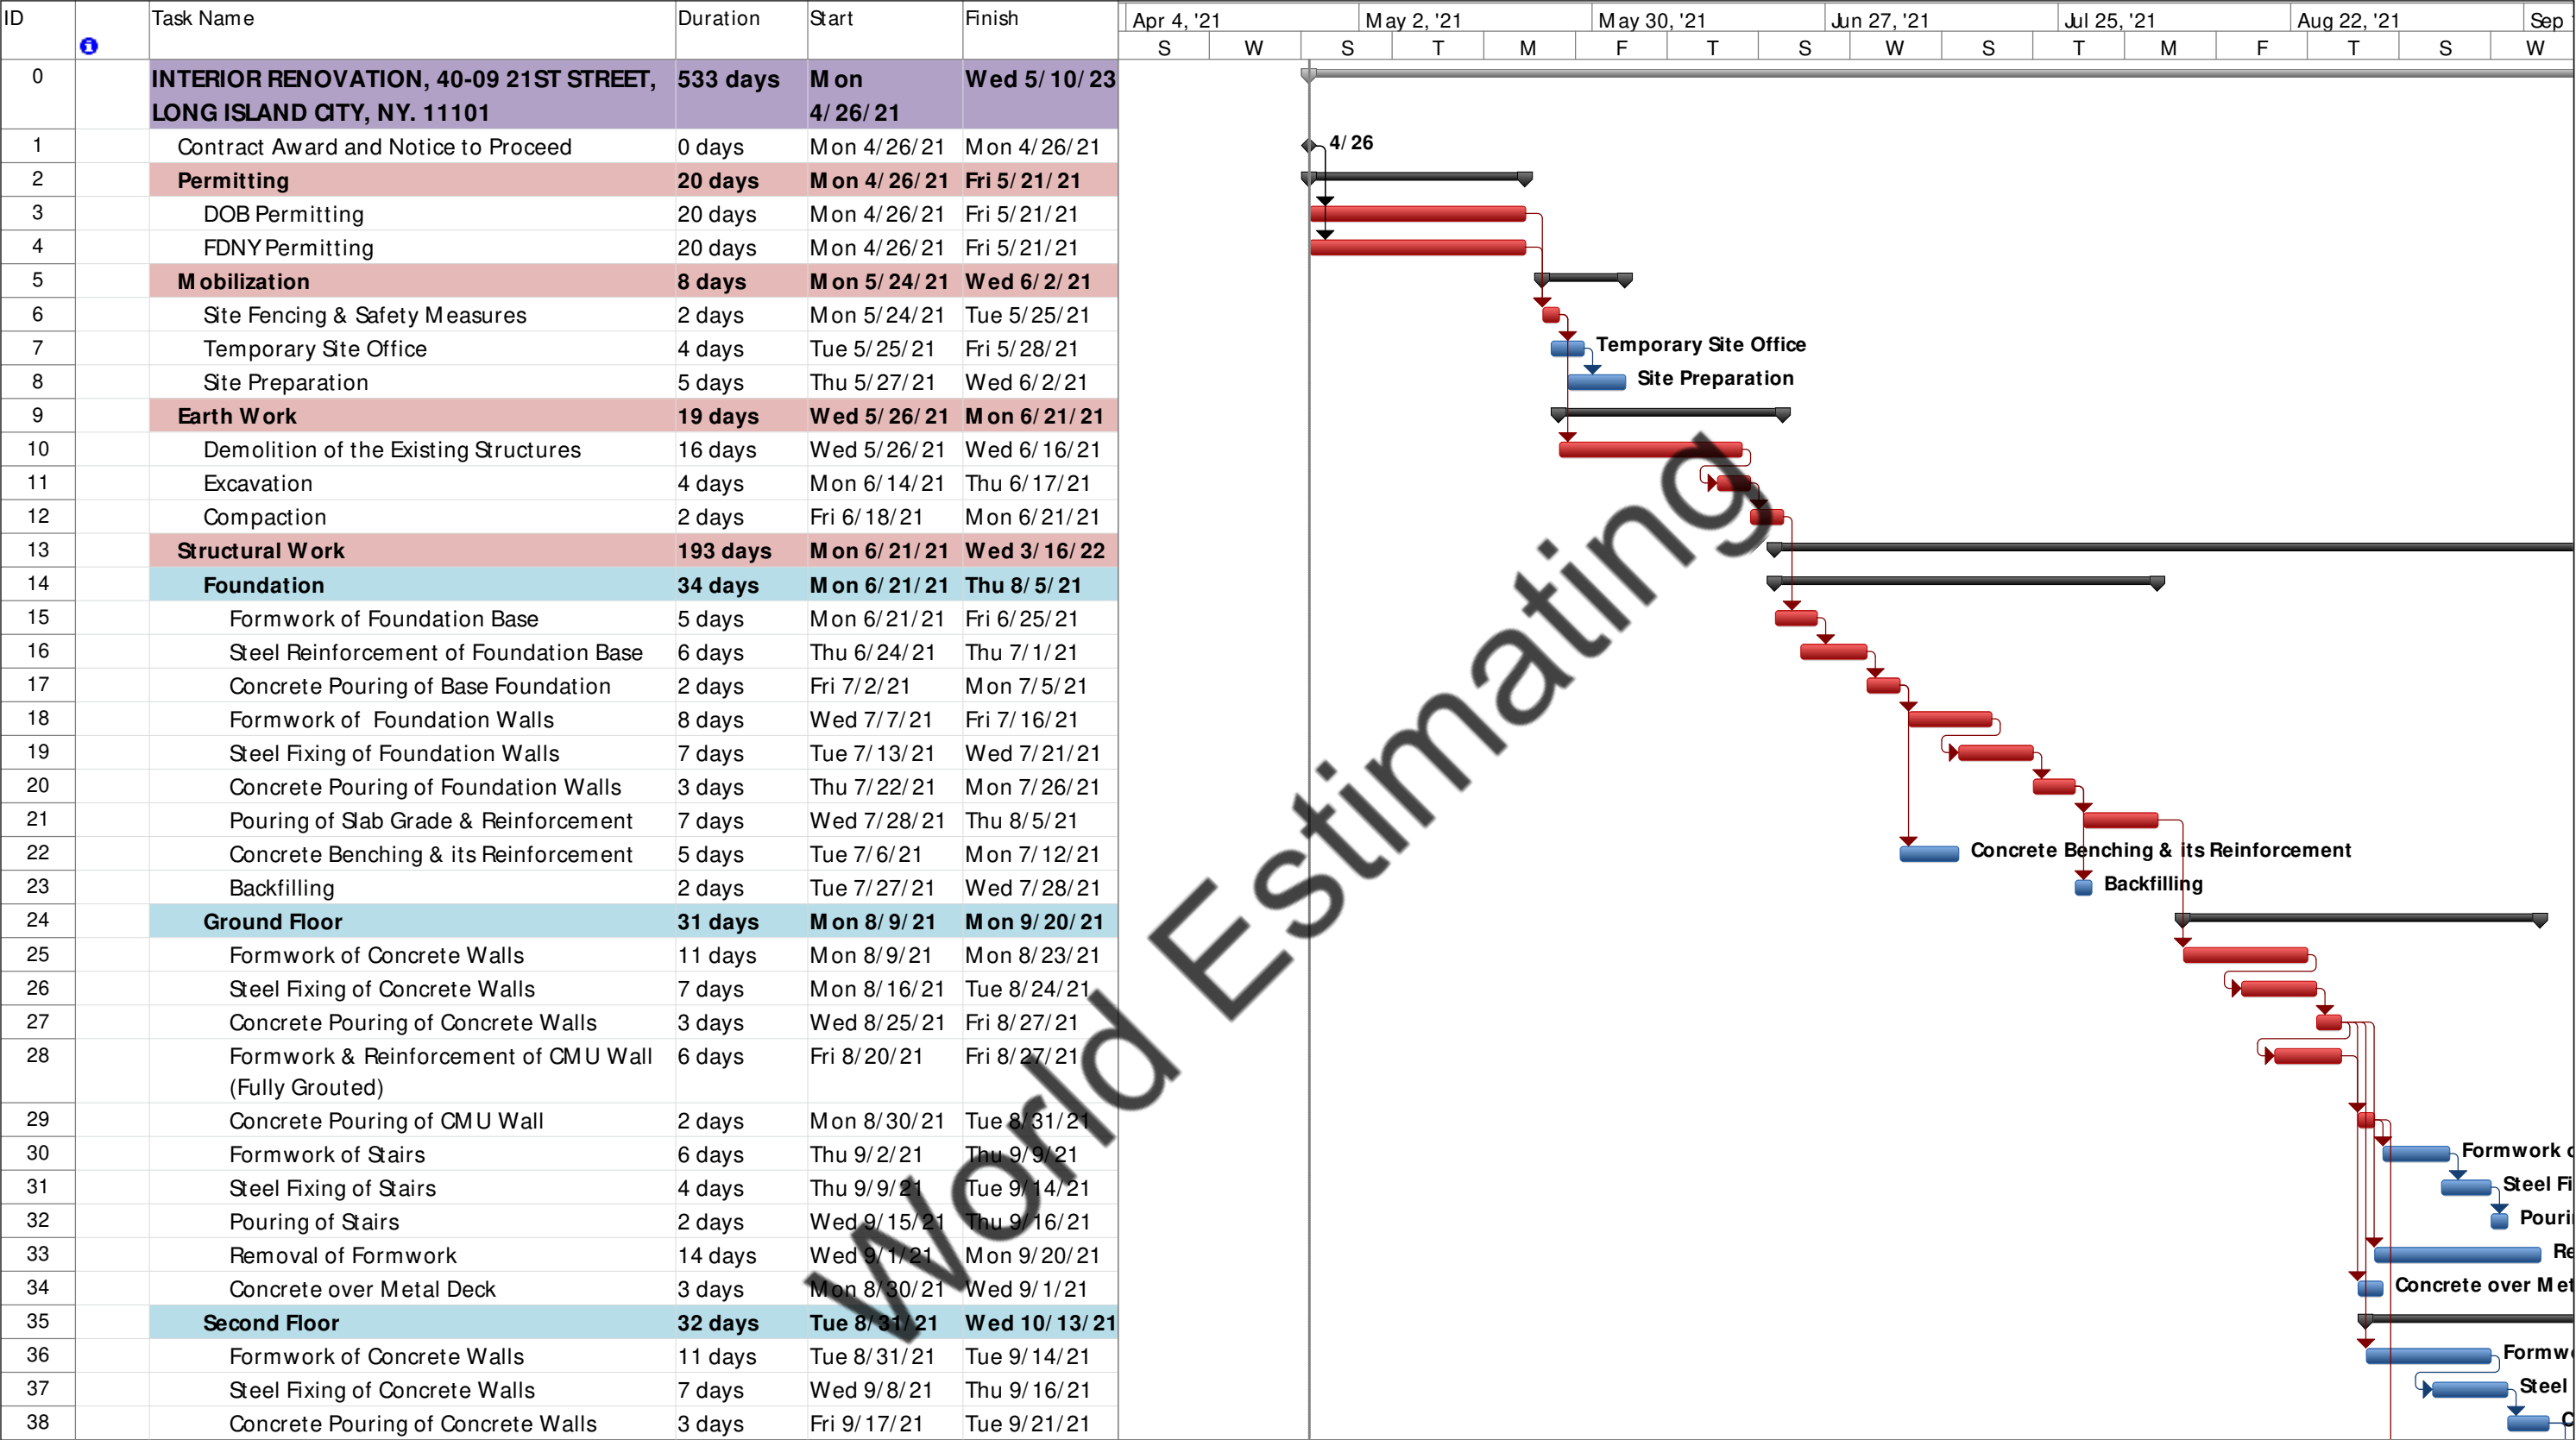

ID	Task Name	Duration	Start	Finish	Apr 4, '21		May 2, '21			May 30, '21			Jun 27, '21		Jul 25, '21			Aug 22, '21		Sep
					S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W
39	Formwork & Reinforcement of CMU Wall (Fully Grouted)	7 days	Fri 9/3/21	Mon 9/13/21																
40	Concrete Pouring of CMU Wall	2 days	Tue 9/14/21	Wed 9/15/21																
41	Formwork of Stairs	6 days	Fri 9/17/21	Fri 9/24/21																
42	Steel Fixing of Stairs	5 days	Fri 9/24/21	Thu 9/30/21																
43	Pouring of Stairs	2 days	Fri 10/1/21	Mon 10/4/21																
44	Removal of Formwork	14 days	Fri 9/24/21	Wed 10/13/21																
45	Third Floor	25 days	Mon 9/20/21	Fri 10/22/21																
46	Formwork of Concrete Walls	12 days	Mon 9/27/21	Tue 10/12/21																
47	Steel Fixing of Concrete Walls	8 days	Wed 10/6/21	Fri 10/15/21																
48	Concrete Pouring of Concrete Walls	3 days	Mon 10/18/21	Wed 10/20/21																
49	Formwork & Reinforcement of CMU Wall (Fully Grouted)	6 days	Mon 9/20/21	Mon 9/27/21																
50	Concrete Pouring of CMU Wall	3 days	Tue 9/28/21	Thu 9/30/21																
51	Formwork of Stairs	6 days	Mon 10/4/21	Mon 10/11/21																
52	Steel Fixing of Stairs	5 days	Mon 10/11/21	Fri 10/15/21																
53	Pouring of Stairs	2 days	Mon 10/18/21	Tue 10/19/21																
54	Removal of Formwork	14 days	Tue 10/5/21	Fri 10/22/21																
55	Fourth Floor	25 days	Fri 10/22/21	Thu 11/25/21																
56	Formwork of Concrete Walls	12 days	Mon 10/25/21	Tue 11/9/21																
57	Steel Fixing of Concrete Walls	8 days	Tue 11/2/21	Thu 11/11/21																
58	Concrete Pouring of Concrete Walls	4 days	Fri 11/12/21	Wed 11/17/21																
59	Formwork & Reinforcement of CMU Wall (Fully Grouted)	6 days	Fri 10/22/21	Fri 10/29/21																
60	Concrete Pouring of CMU Wall	3 days	Mon 11/1/21	Wed 11/3/21																
61	Formwork of Stairs	7 days	Fri 11/5/21	Mon 11/15/21																
62	Steel Fixing of Stairs	6 days	Fri 11/12/21	Fri 11/19/21																
63	Pouring of Stairs	2 days	Mon 11/22/21	Tue 11/23/21																
64	Removal of Formwork	14 days	Mon 11/8/21	Thu 11/25/21																
65	Fifth Floor	27 days	Mon 11/22/21	Tue 12/28/21																
66	Formwork of Concrete Walls	13 days	Mon 11/22/21	Wed 12/8/21																
67	Steel Fixing of Concrete Walls	8 days	Wed 12/1/21	Fri 12/10/21																
68	Concrete Pouring of Concrete Walls	3 days	Mon 12/13/21	Wed 12/15/21																
69	Formwork & Reinforcement of CMU Wall (Fully Grouted)	6 days	Thu 11/25/21	Thu 12/2/21																
70	Concrete Pouring of CMU Wall	2 days	Fri 12/3/21	Mon 12/6/21																
71	Formwork of Stairs	6 days	Thu 12/9/21	Thu 12/16/21																
72	Steel Fixing of Stairs	5 days	Wed 12/15/21	Tue 12/21/21																
73	Pouring of Stairs	2 days	Wed 12/22/21	Thu 12/23/21																
74	Removal of Formwork	14 days	Thu 12/9/21	Tue 12/28/21																
75	Sixth Floor	28 days	Thu 12/9/21	Mon 1/17/22																
76	Formwork of Concrete Walls	13 days	Mon 12/20/21	Wed 1/5/22																
77	Steel Fixing of Concrete Walls	8 days	Thu 12/30/21	Mon 1/10/22																

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Critical

Critical Split

Progress

ID		Task Name	Duration	Start	Finish	Apr 4, '21			May 2, '21			May 30, '21			Jun 27, '21			Jul 25, '21			Aug 22, '21			Sep
						S	W		S	T	M	F	T	S	W	S	T	M	F	T	S	W		
119		Ceiling	45 days	Tue 4/ 19/ 22	Mon 6/ 20/ 22																			
120		Stairs Railing	18 days	Wed 6/ 1/ 22	Fri 6/ 24/ 22																			
121		Reception Desks	8 days	Thu 6/ 16/ 22	Mon 6/ 27/ 22																			
122		Plumbing Work	163 days	Wed 12/ 8/ 21	Fri 7/ 22/ 22																			
123		Sanitary Piping and Fittings	18 days	Tue 5/ 17/ 22	Thu 6/ 9/ 22																			
124		Storm Water Pipings and Fittings	9 days	Thu 6/ 2/ 22	Tue 6/ 14/ 22																			
125		Gas Pipings and Fittings	66 days	Wed 12/ 8/ 21	Wed 3/ 9/ 22																			
126		Installation of Water Lines	65 days	Tue 12/ 14/ 21	Mon 3/ 14/ 22																			
127		Supplying & Installation of Pumps	10 days	Wed 6/ 15/ 22	Tue 6/ 28/ 22																			
128		Installation of W.Cs	15 days	Thu 6/ 23/ 22	Wed 7/ 13/ 22																			
129		Installation of Vanities	17 days	Thu 6/ 30/ 22	Fri 7/ 22/ 22																			
130		Openings	35 days	Thu 6/ 9/ 22	Wed 7/ 27/ 22																			
131		Supplying & Installation of Doors	35 days	Thu 6/ 9/ 22	Wed 7/ 27/ 22																			
132		Supplying & Installation of Windows	22 days	Tue 6/ 28/ 22	Wed 7/ 27/ 22																			
133		Electrical Work	217 days	Fri 1/ 7/ 22	Mon 11/ 7/ 22																			
134		Conduiting and Fittings	160 days	Fri 1/ 7/ 22	Thu 8/ 18/ 22																			
135		Outlets & Switches	37 days	Fri 7/ 22/ 22	Mon 9/ 12/ 22																			
136		Distribution Board Pannels	15 days	Fri 9/ 2/ 22	Thu 9/ 22/ 22																			
137		Lighting Fixtures	40 days	Tue 9/ 13/ 22	Mon 11/ 7/ 22																			
138		Mechanical Work	66 days	Thu 9/ 15/ 22	Thu 12/ 15/ 22																			
139		Supplying & Installation of Ceiling Mounted/ Split A/ C Units	50 days	Thu 9/ 15/ 22	Wed 11/ 23/ 22																			
140		Refrigerant Pipes	37 days	Tue 10/ 25/ 22	Wed 12/ 14/ 22																			
141		Installation of Elevators	45 days	Fri 10/ 14/ 22	Thu 12/ 15/ 22																			
142		Closeout	104 days	Fri 12/ 16/ 22	Wed 5/ 10/ 23																			
143		Testing & Commisioning	35 days	Fri 12/ 16/ 22	Thu 2/ 2/ 23																			
144		Final Cleaning	7 days	Fri 1/ 27/ 23	Mon 2/ 6/ 23																			
145		Final Inspection	5 days	Fri 2/ 3/ 23	Thu 2/ 9/ 23																			
146		Temporary Certificate of Occupancy	15 days	Wed 2/ 8/ 23	Tue 2/ 28/ 23																			
147		Completion of Punch list Items	35 days	Wed 2/ 8/ 23	Tue 3/ 28/ 23																			
148		Final Certificate of Occupancy	35 days	Wed 3/ 22/ 23	Tue 5/ 9/ 23																			
149		Final Sign-Off	30 days	Thu 3/ 30/ 23	Wed 5/ 10/ 23																			
150		Handing/ Turning Over	0 days	Wed 5/ 10/ 23	Wed 5/ 10/ 23																			



Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Critical

Critical Split

Progress


Sep 19, '21			Oct 17, '21			Nov 14, '21			Dec 12, '21			Jan 9, '22			Feb 6, '22			Mar 6, '22			Apr 3, '22			May 1, '22			May 29, '22			Jun 26, '22		
W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S					

- Formwork of Stairs
- Steel Fixing of Stairs
- Pouring of Stairs
- Removal of Formwork
- over Metal Deck
- Formwork of Concrete Walls
- Steel Fixing of Concrete Walls
- Concrete Pouring of Concrete Walls


G

G-FOUR

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Critical	
Milestone		External Milestone		Manual Task		Start-only		Critical Split	
Summary		Inactive Task		Duration-only		Finish-only		Progress	

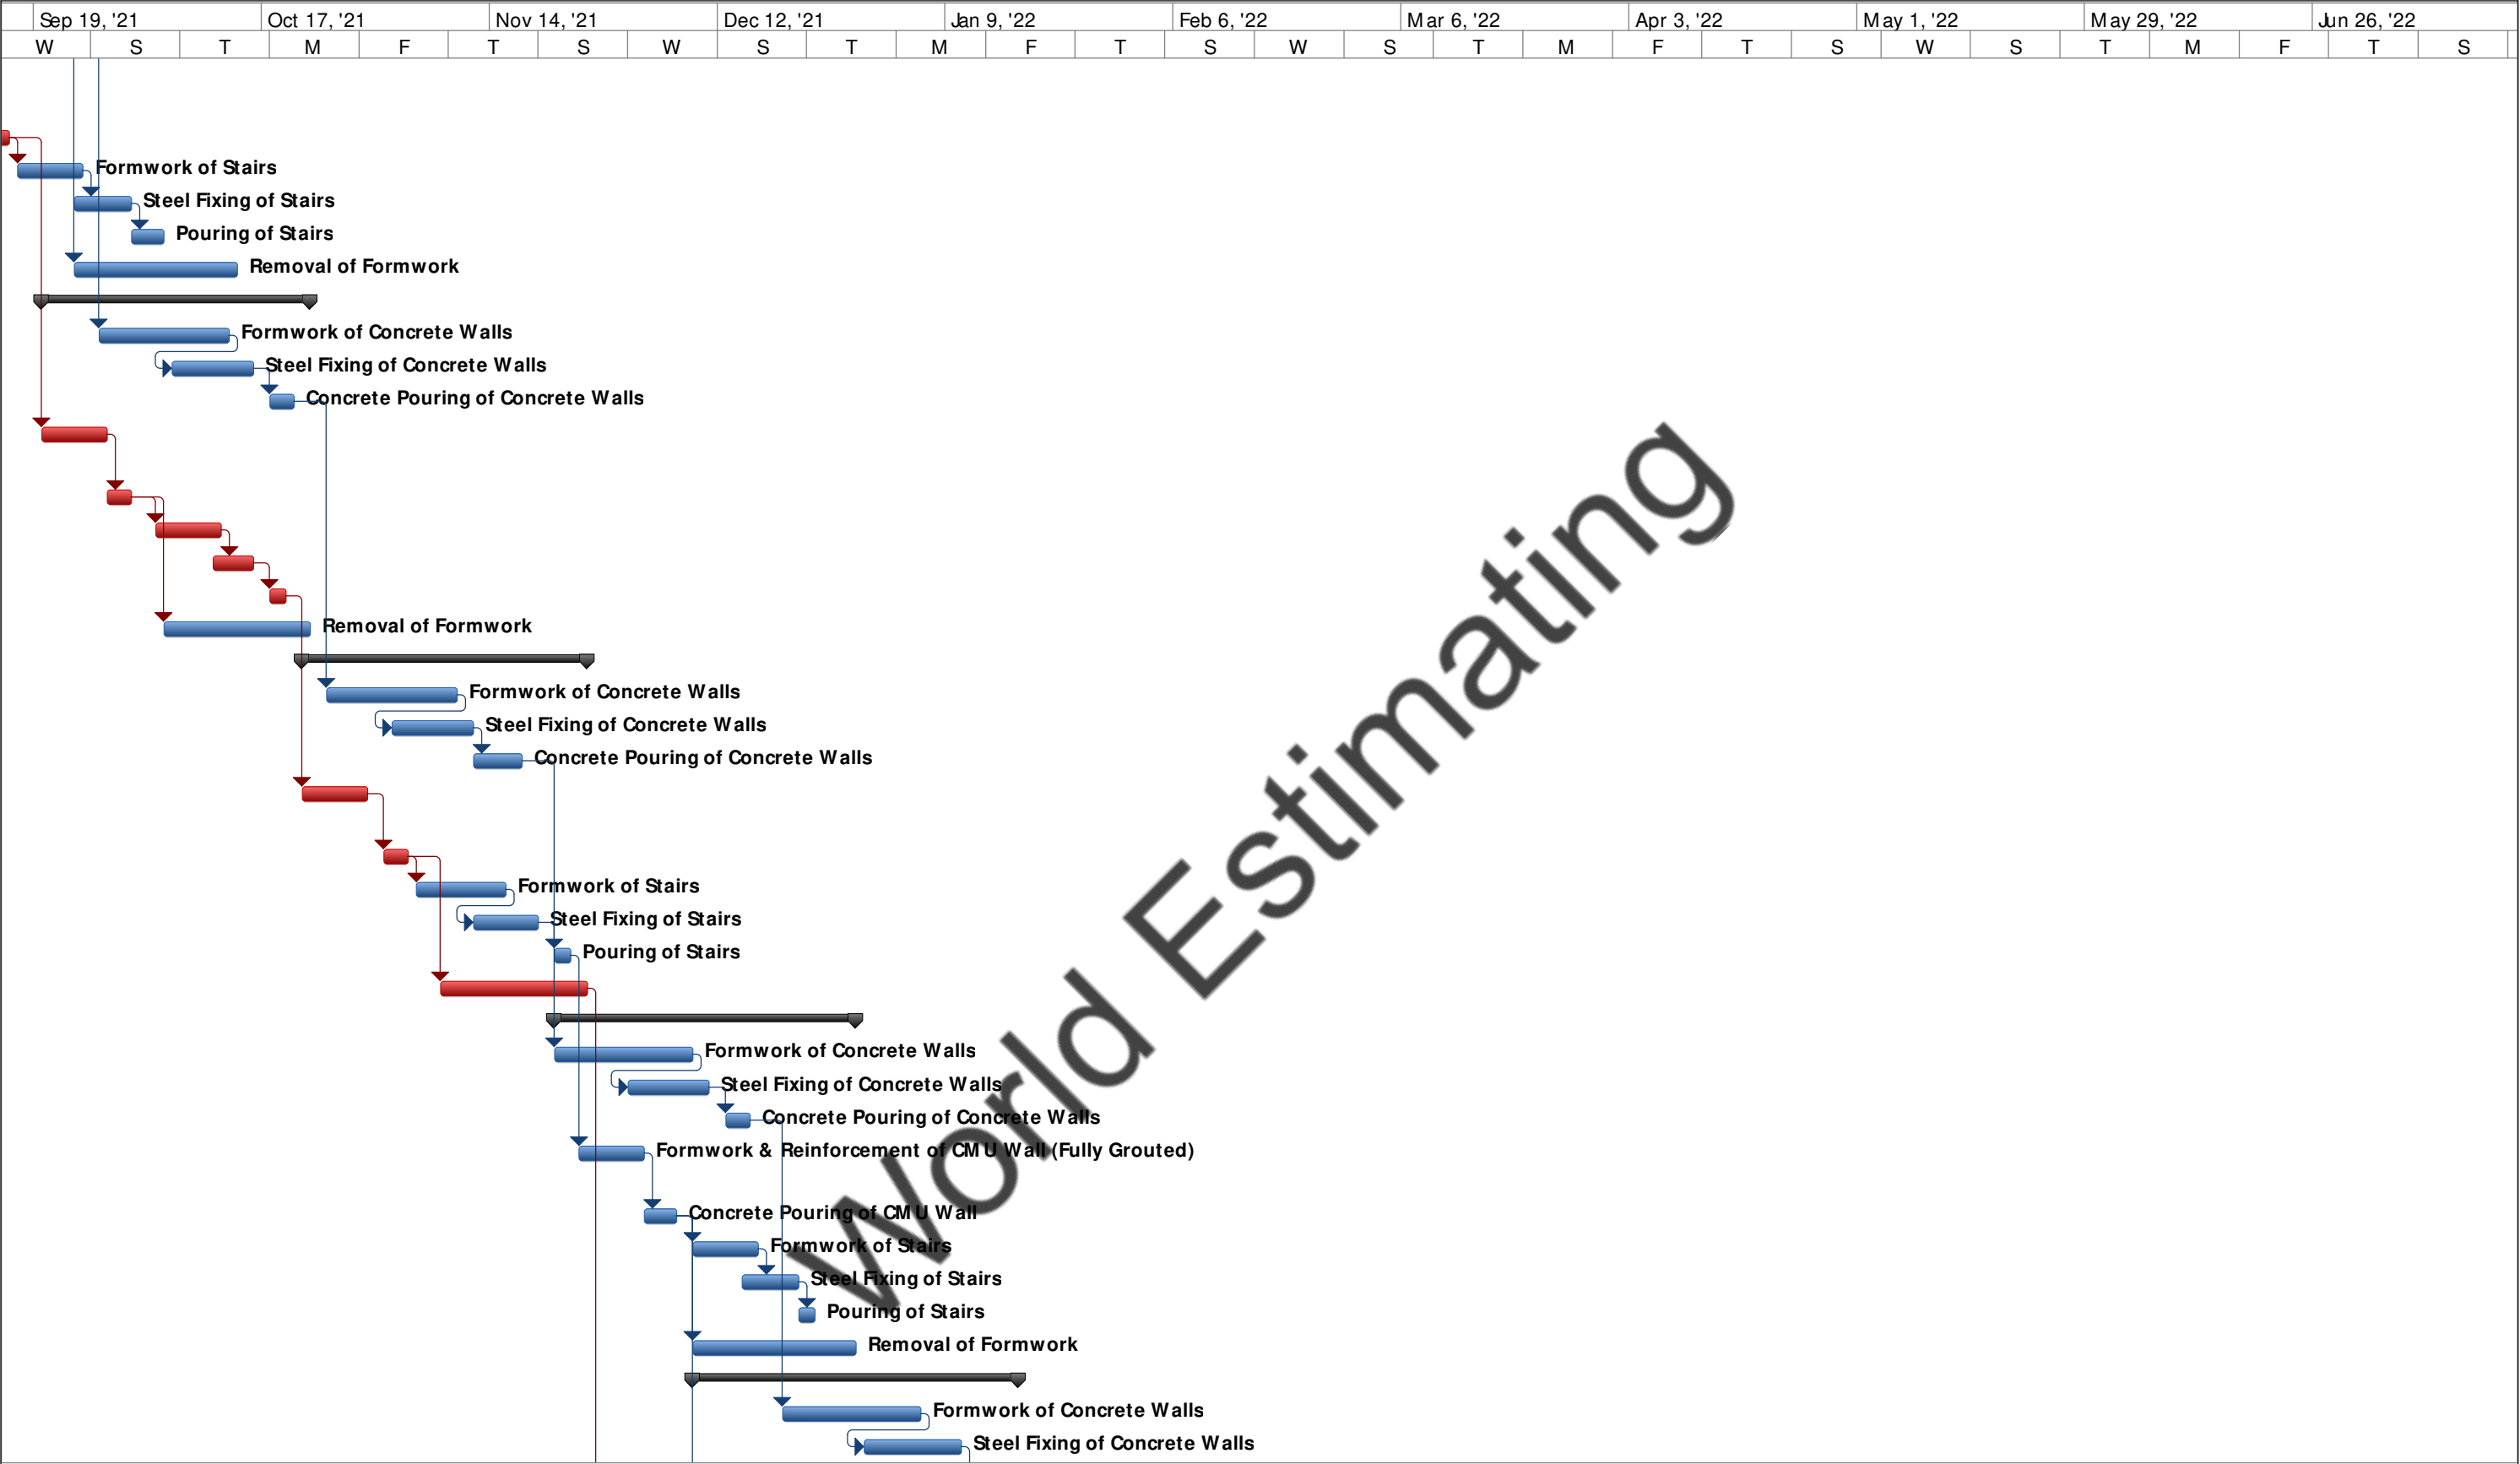


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Critical	
Milestone		External Milestone		Manual Task		Start-only		Critical Split	
Summary		Inactive Task		Duration-only		Finish-only		Progress	

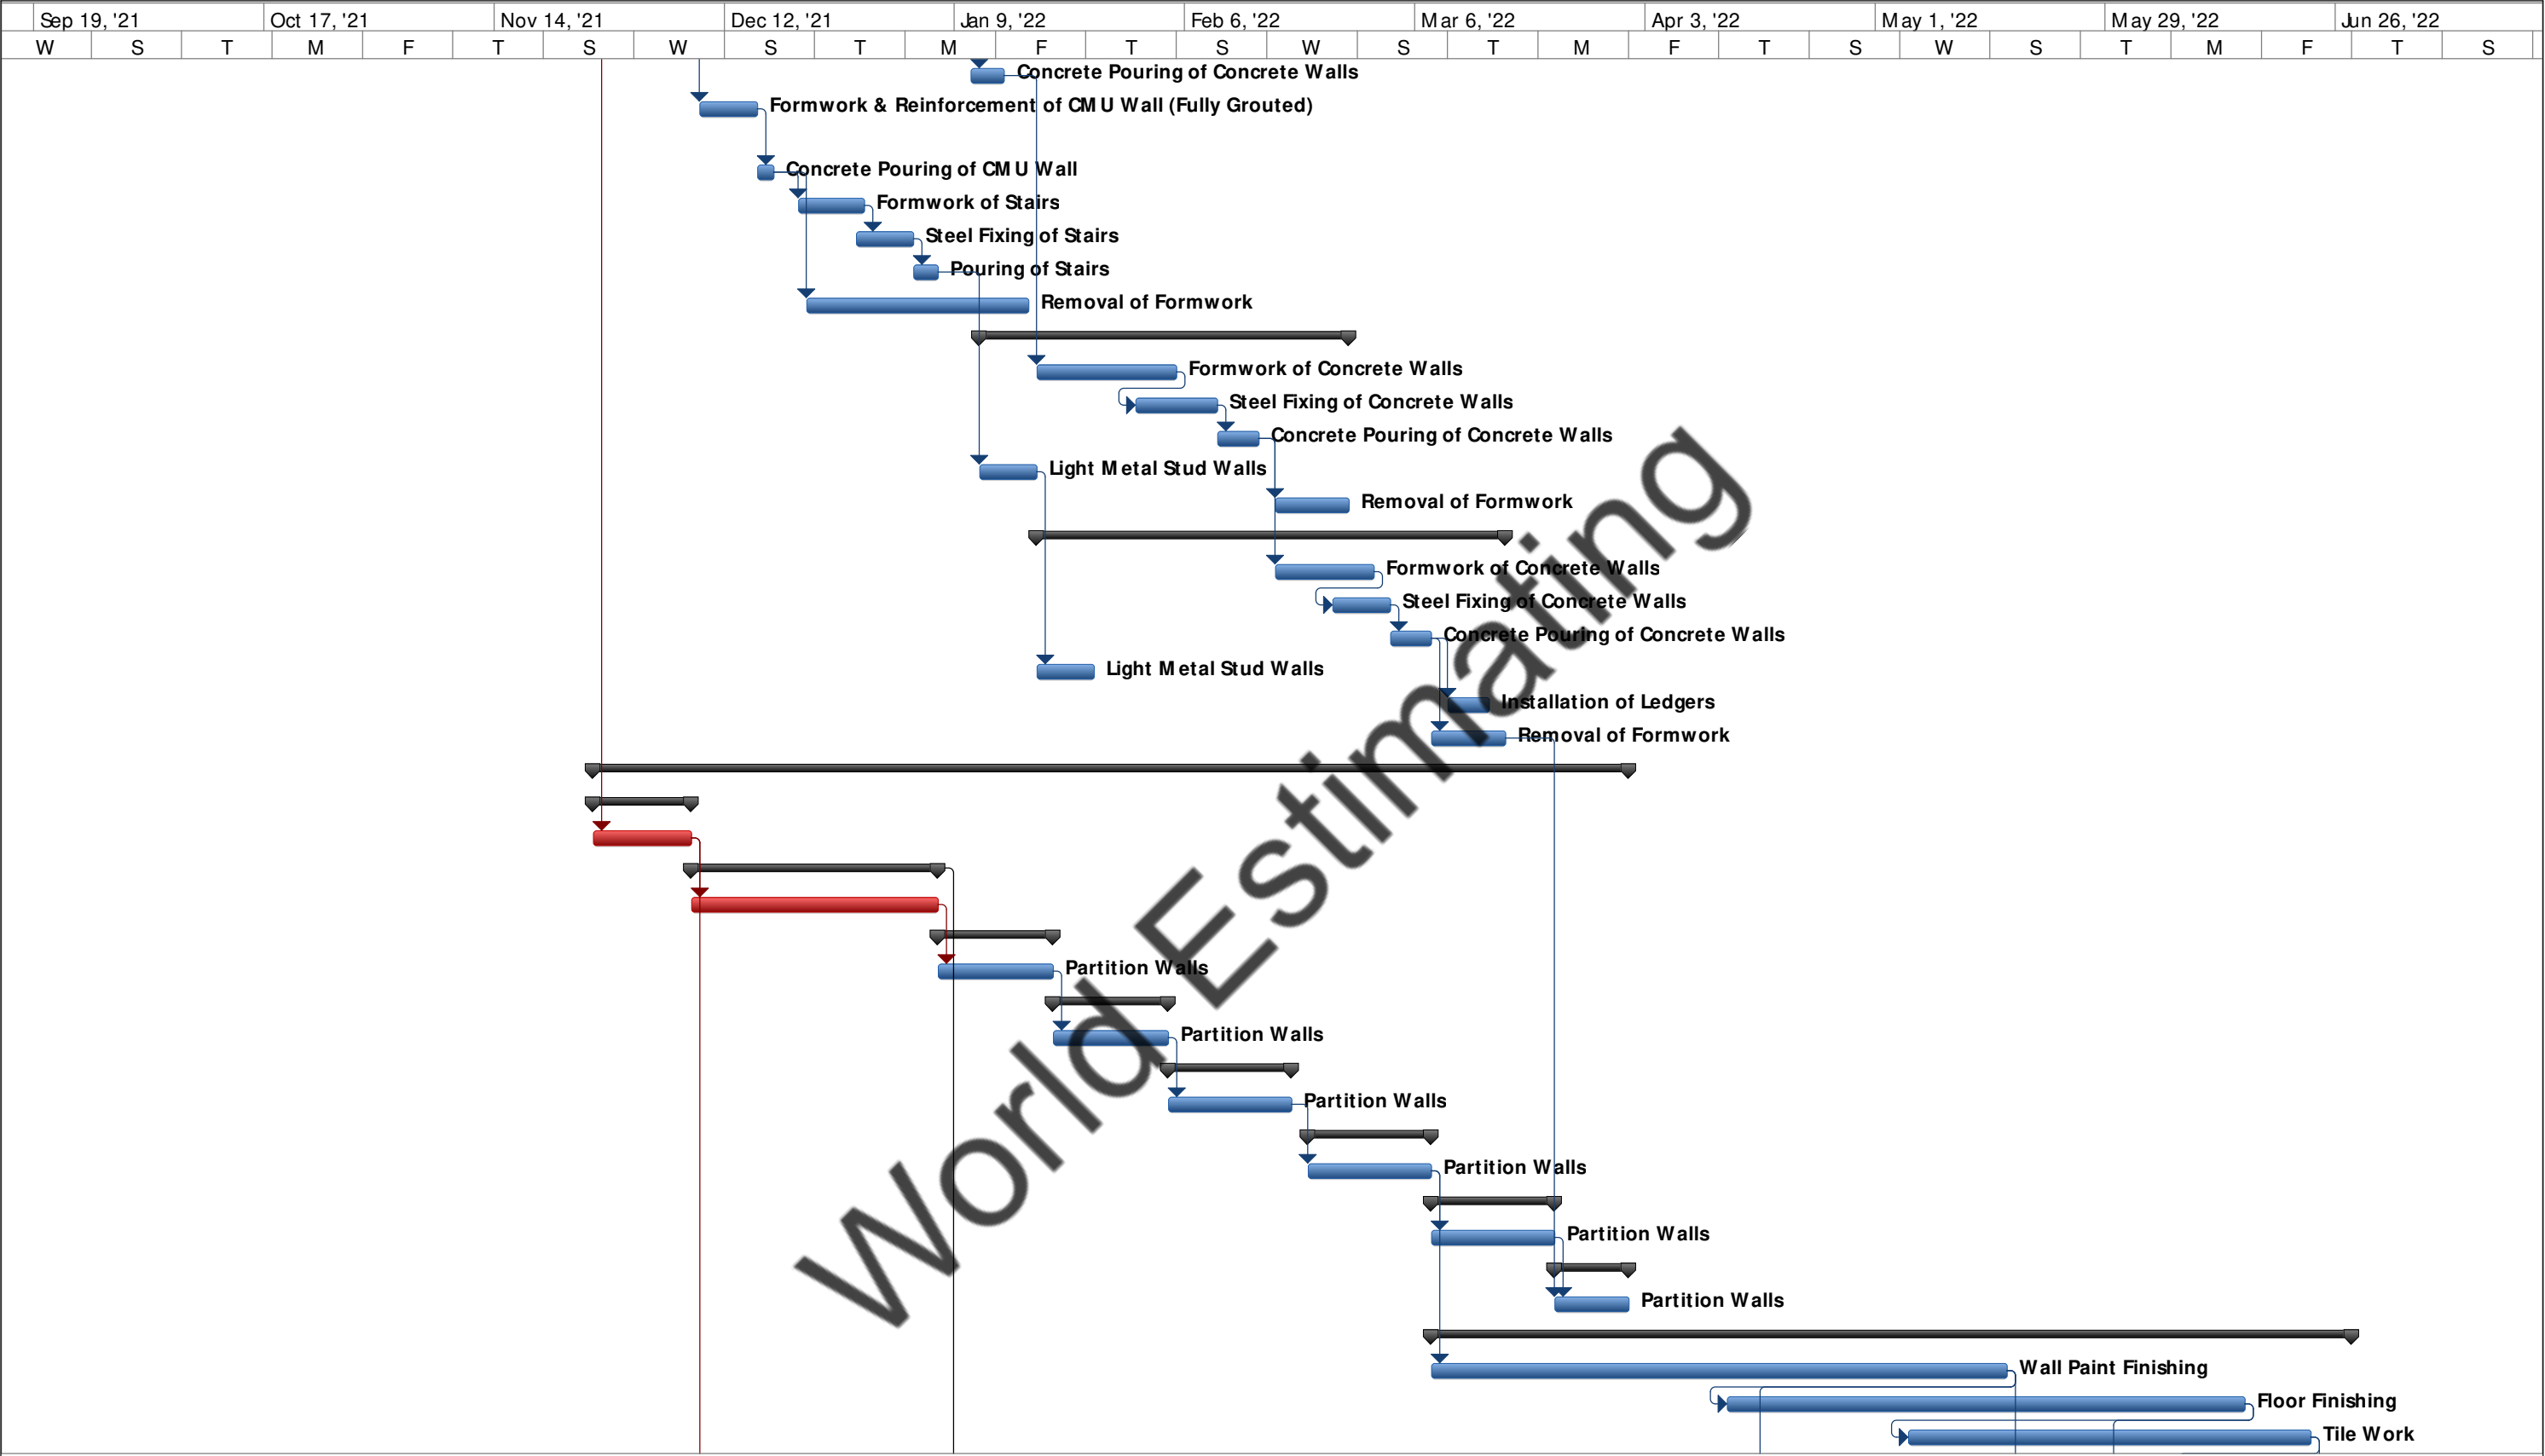


	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	

Sep 19, '21			Oct 17, '21			Nov 14, '21			Dec 12, '21			Jan 9, '22			Feb 6, '22			Mar 6, '22			Apr 3, '22			May 1, '22			May 29, '22			Jun 26, '22		
W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S					

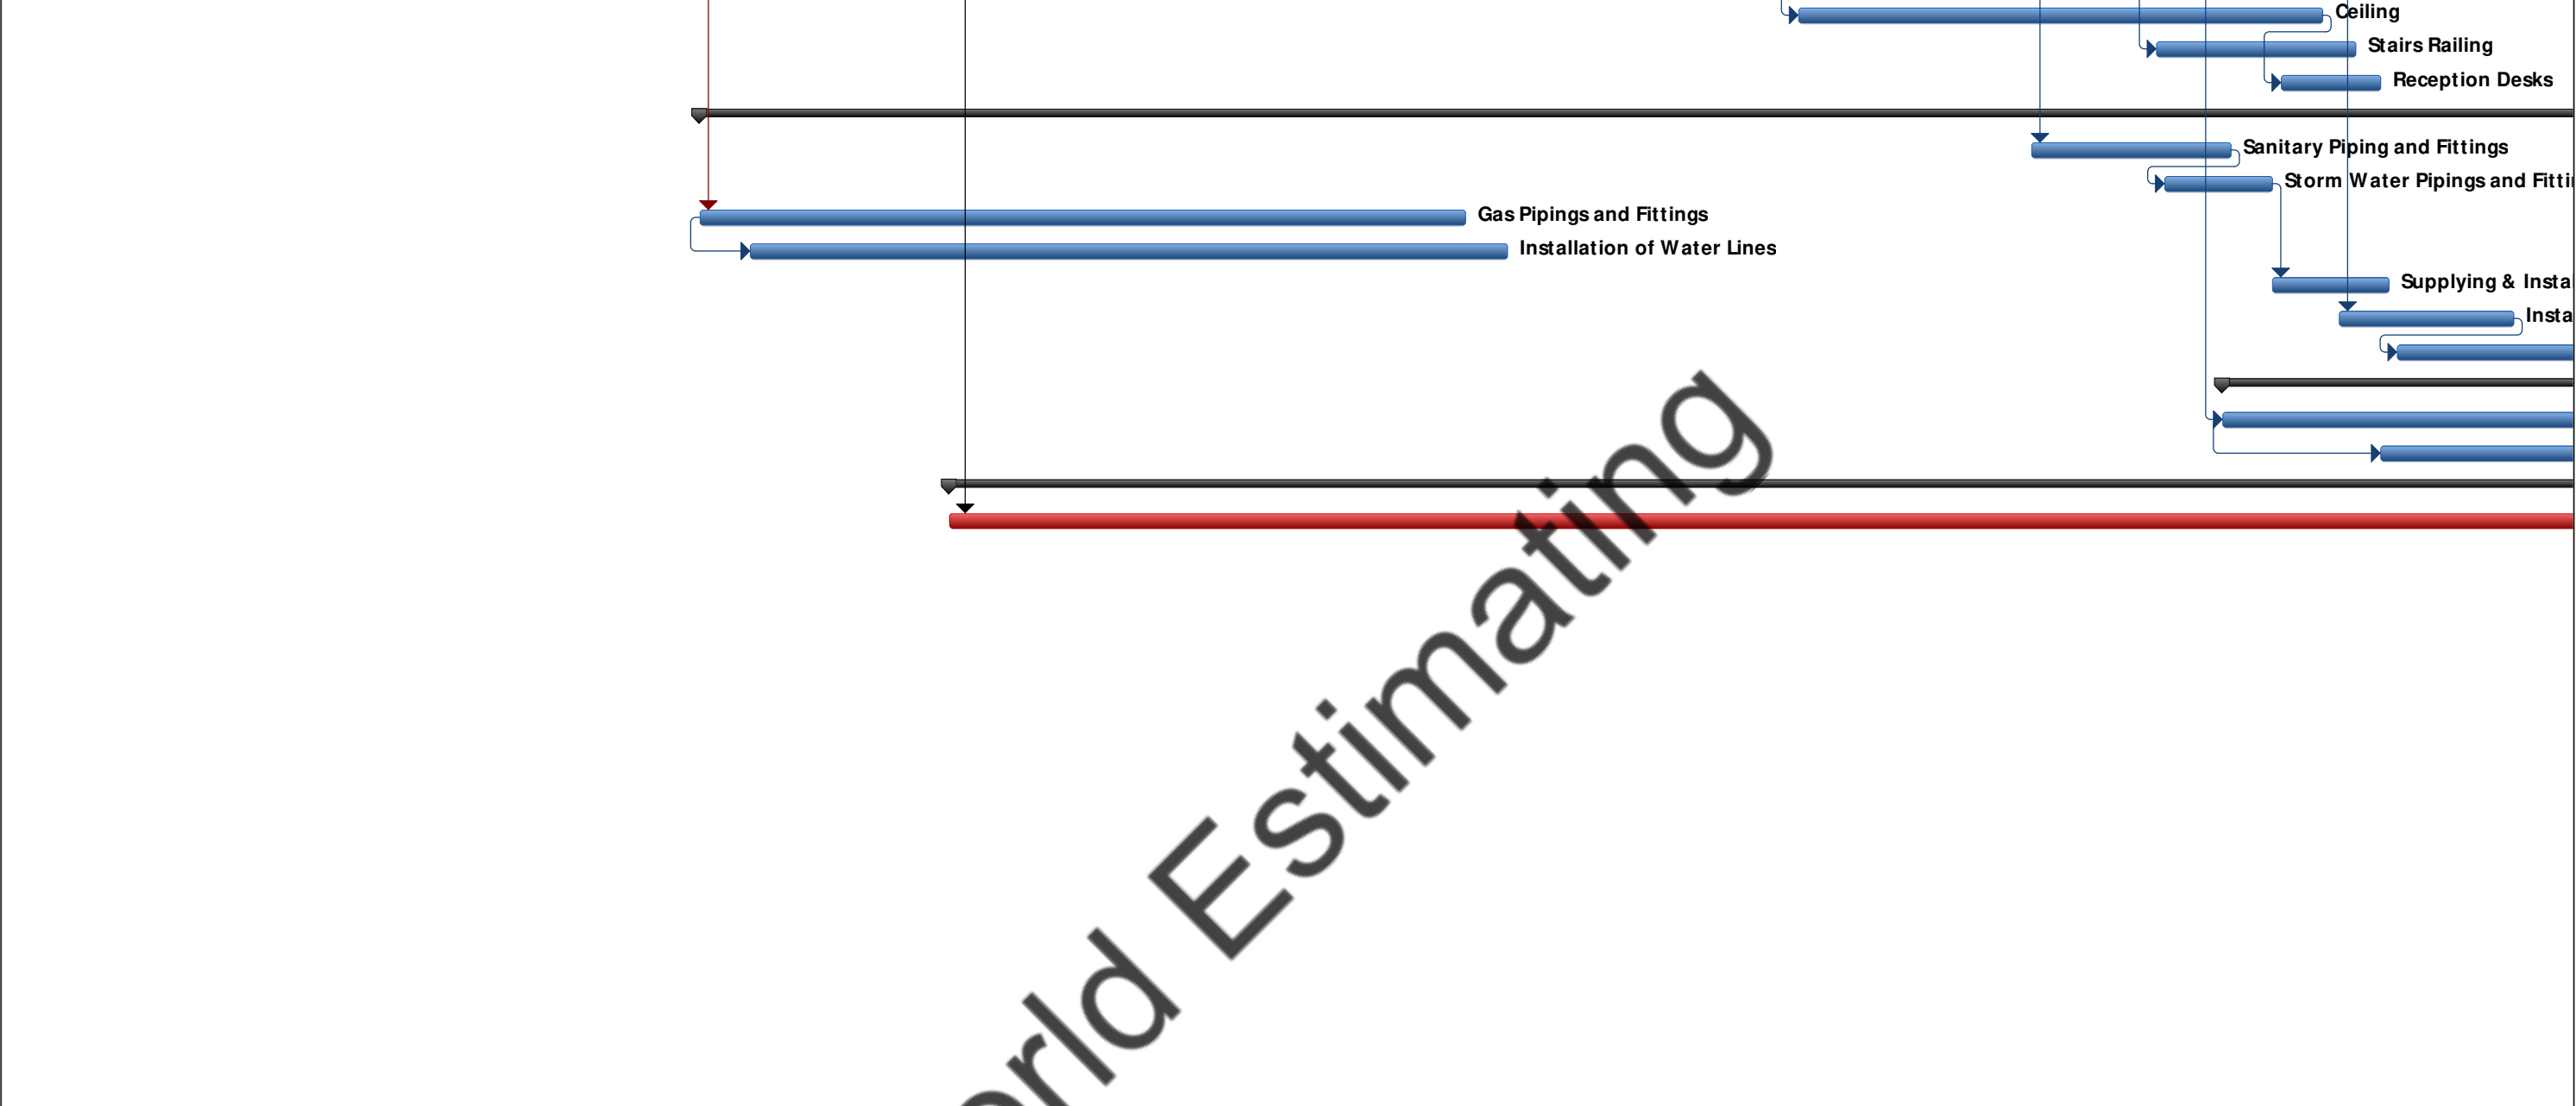

	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	

Jul 24, '22			Aug 21, '22			Sep 18, '22			Oct 16, '22			Nov 13, '22			Dec 11, '22			Jan 8, '23			Feb 5, '23			Mar 5, '23			Apr 2, '23			Apr 30, '23		
W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S					

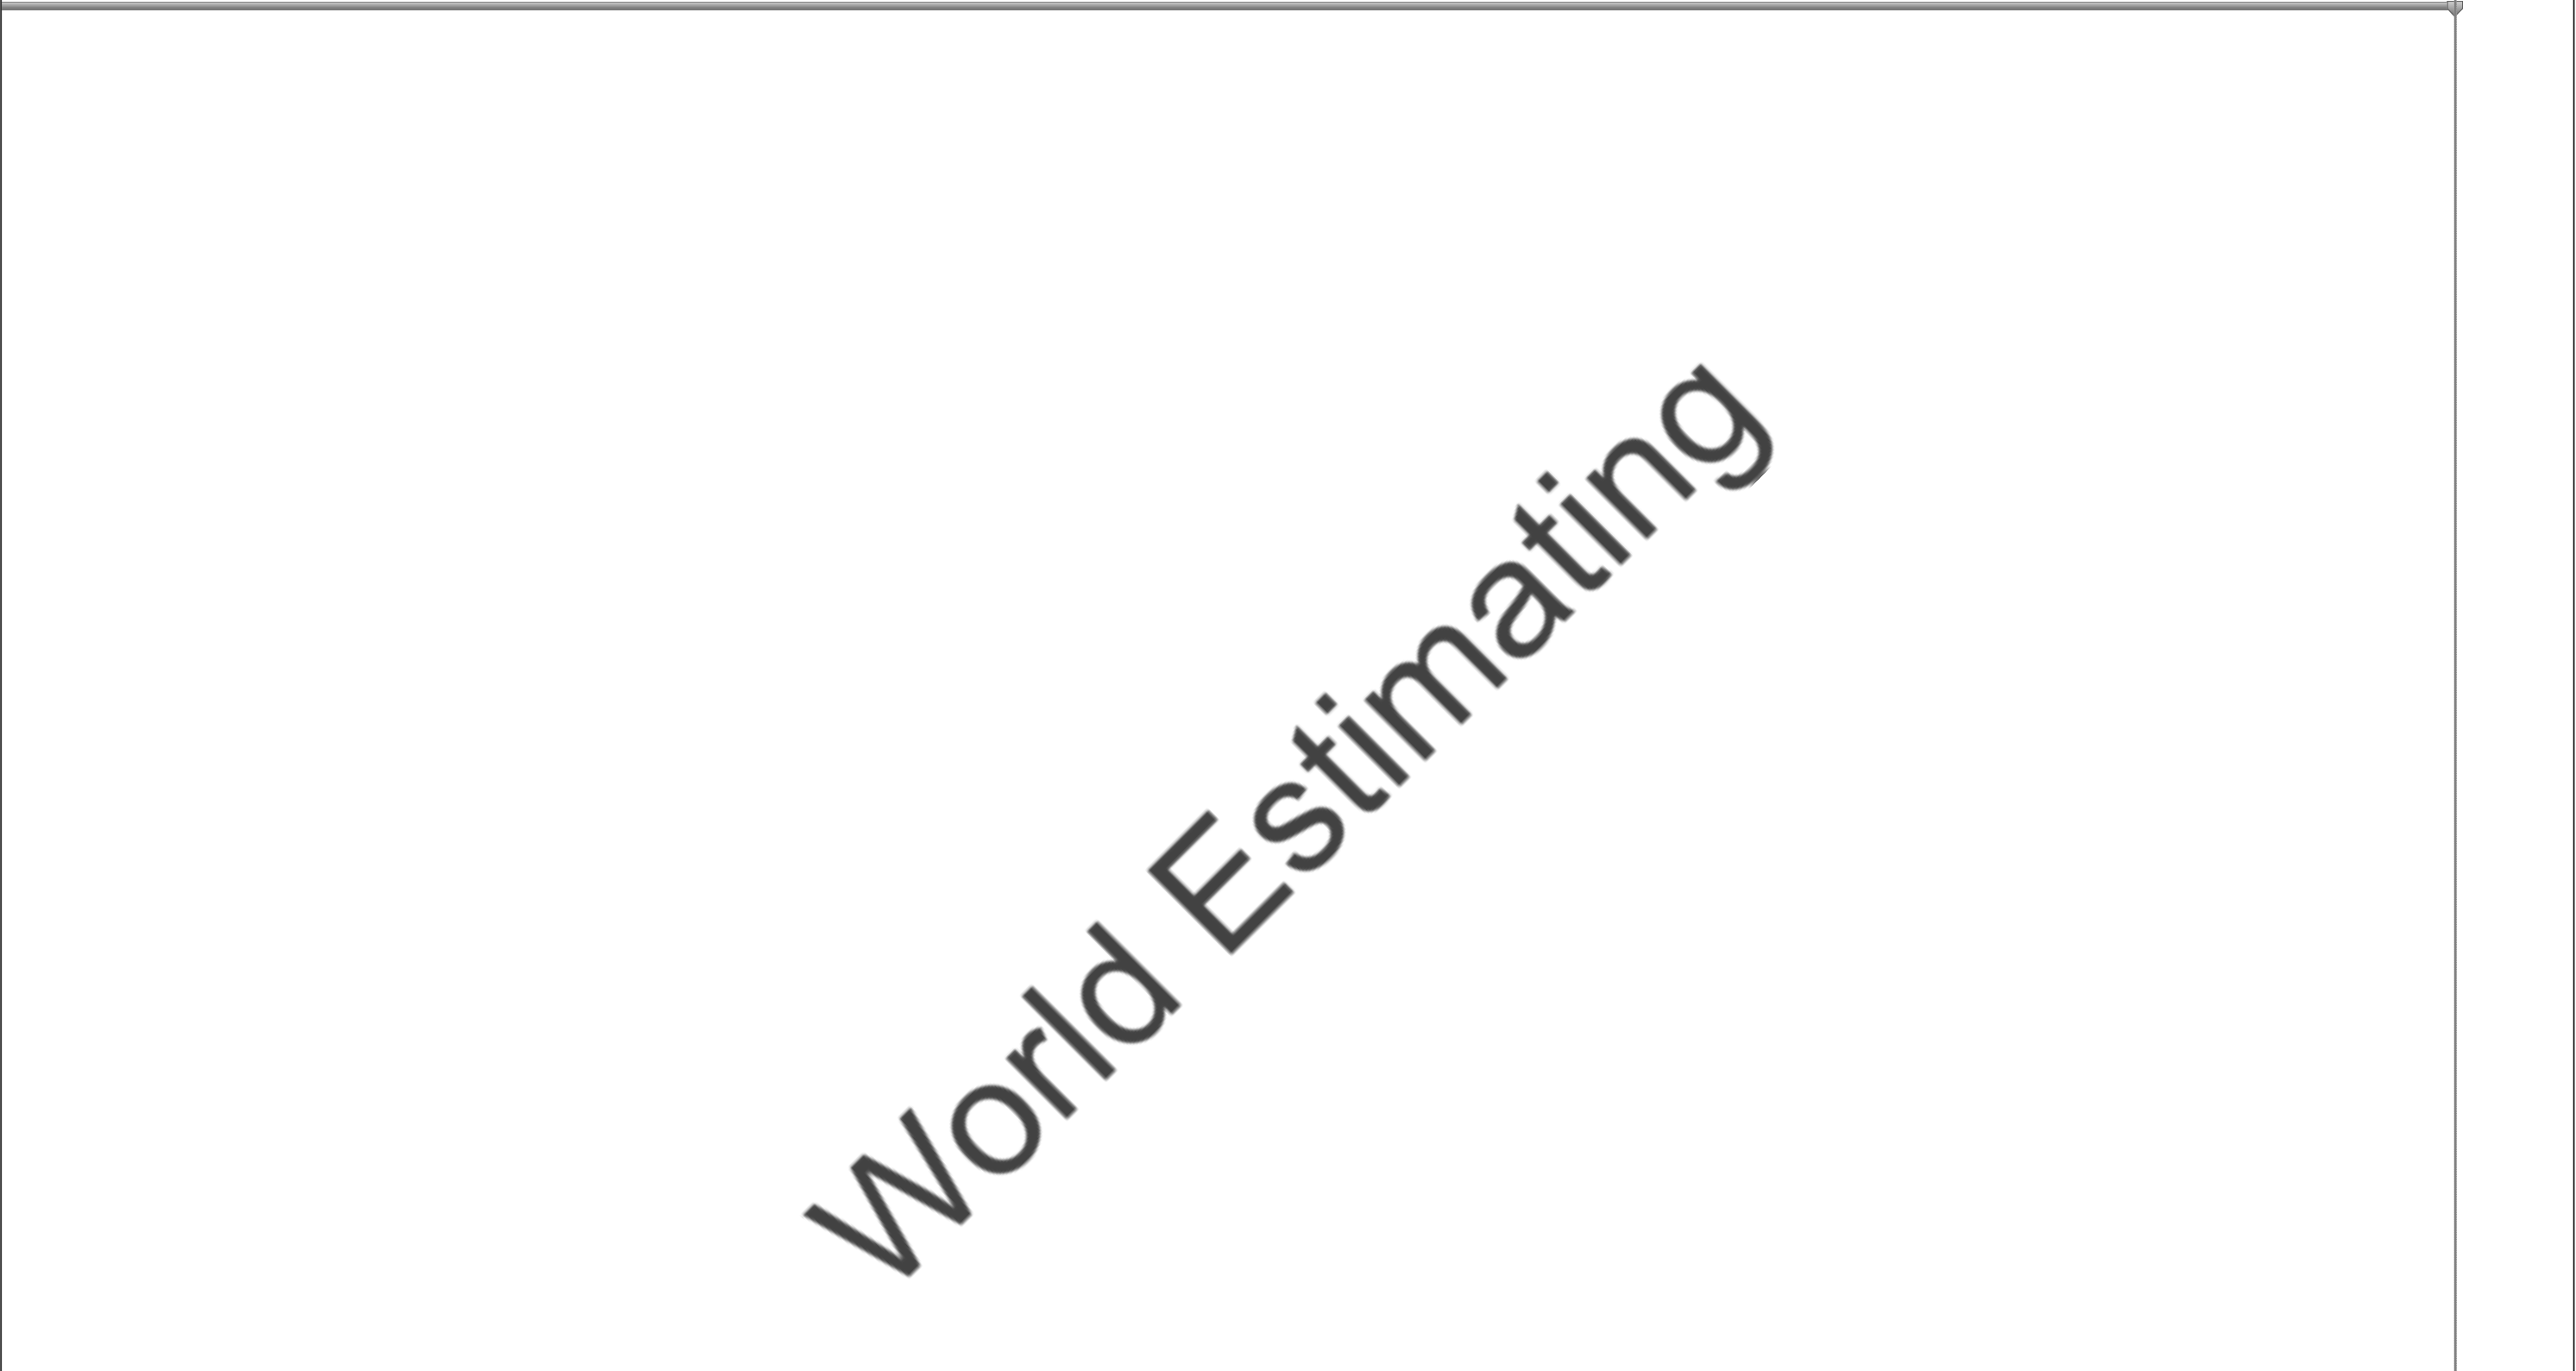

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Critical	
Milestone		External Milestone		Manual Task		Start-only		Critical Split	
Summary		Inactive Task		Duration-only		Finish-only		Progress	

Jul 24, '22			Aug 21, '22			Sep 18, '22			Oct 16, '22			Nov 13, '22			Dec 11, '22			Jan 8, '23			Feb 5, '23			Mar 5, '23			Apr 2, '23			Apr 30, '23		
W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S					



Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Critical	
Milestone		External Milestone		Manual Task		Start-only		Critical Split	
Summary		Inactive Task		Duration-only		Finish-only		Progress	

Jul 24, '22			Aug 21, '22			Sep 18, '22			Oct 16, '22			Nov 13, '22			Dec 11, '22			Jan 8, '23			Feb 5, '23			Mar 5, '23			Apr 2, '23			Apr 30, '23		
W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S					





Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Critical	
Milestone		External Milestone		Manual Task		Start-only		Critical Split	
Summary		Inactive Task		Duration-only		Finish-only		Progress	

Jul 24, '22			Aug 21, '22			Sep 18, '22			Oct 16, '22			Nov 13, '22			Dec 11, '22			Jan 8, '23			Feb 5, '23			Mar 5, '23			Apr 2, '23			Apr 30, '23		
W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S					

Settings


Installation of Pumps

Installation of W.Cs

Installation of Vanities

Supplying & Installation of Doors

Supplying & Installation of Windows

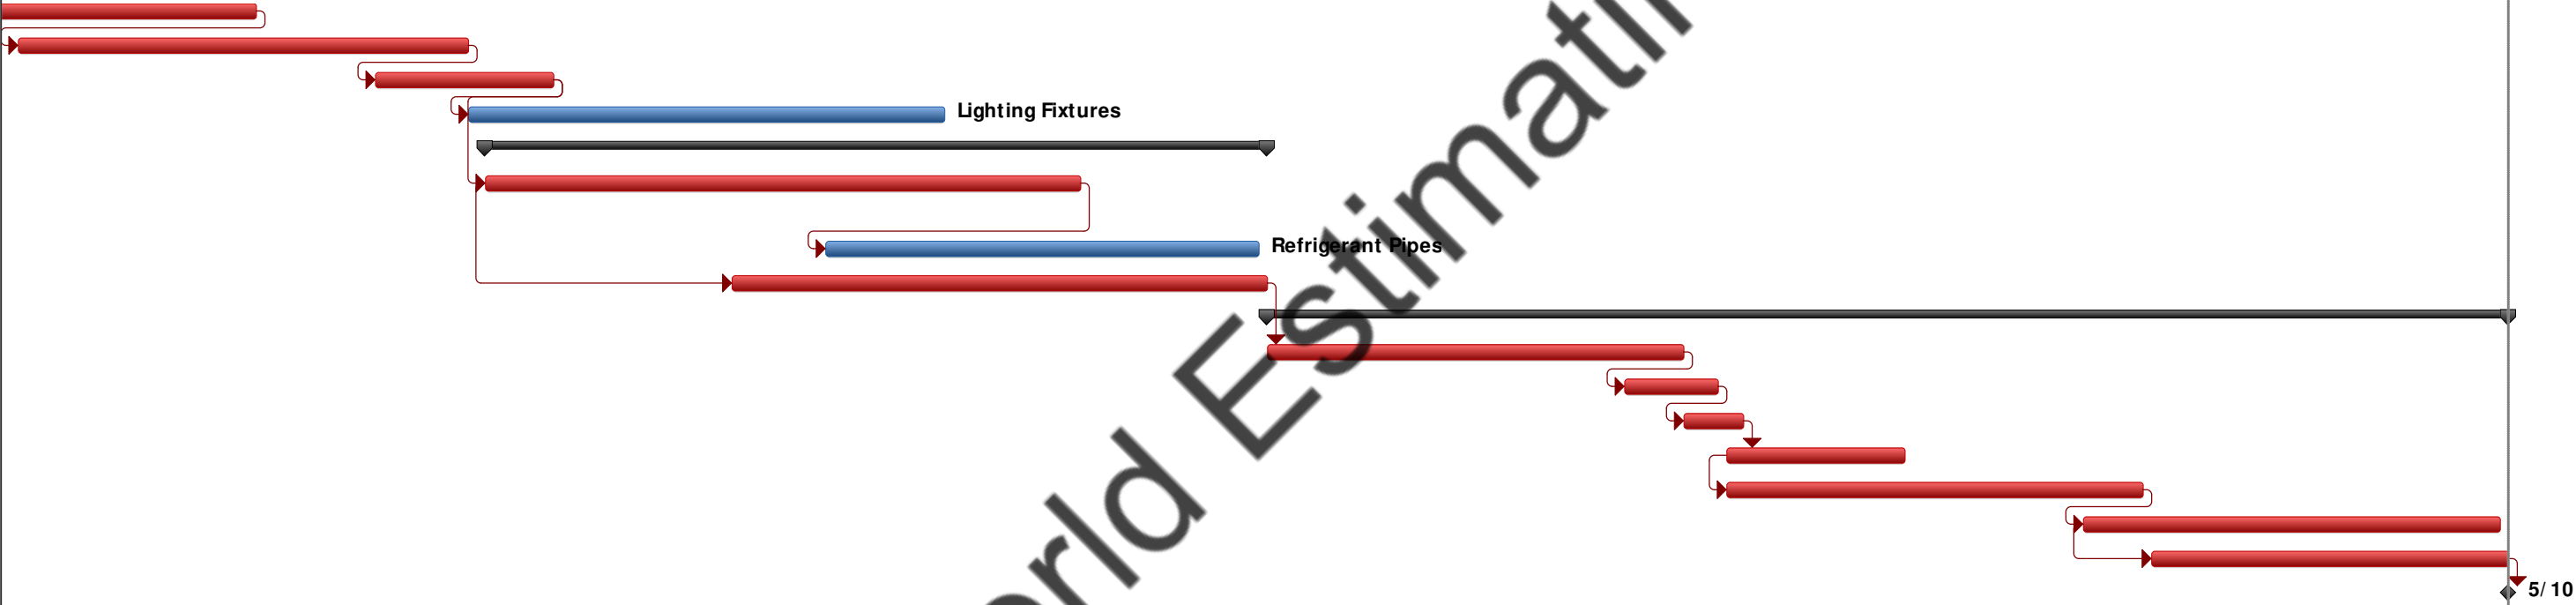

	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Critical	
	Milestone		External Milestone		Manual Task		Start-only		Critical Split	
	Summary		Inactive Task		Duration-only		Finish-only		Progress	
